



PROJECT UPDATE

Silvergate Rancho Bernardo
San Diego, CA

September 2018



TABLE OF CONTENTS

- Current Highlights
- Upcoming Schedule Milestones
- Safe Hours
- Project Photos
- Virtual Design Coordination
- Time-Lapse
- Upcoming Highlights
- Ryan Companies Contact Information



CURRENT HIGHLIGHTS

- East Apartments (Building 6)
 - S foundation reinforcement and pour complete (9/27)
 - N foundation reinforcement in progress
- Podium Deck (Buildings 1 & 2)
 - Slab pour complete (9/12)
- Memory Care (Building 2)
 - Structural steel and panelized wall erection in progress
 - Steel fire retardant paint application in progress
- West Apartments (Building 5)
 - S foundation reinforcement in progress
 - N foundation excavation in progress
- E Cottages (7D, 7E, 8C, 8D, 9B)
 - Grading complete. Foundation excavation and UG plumbing in progress
- Clubhouse (Building 4)
 - Rough grading complete. UG plumbing & electrical in progress
 - Slab on Gra

Fun Fact:

- 5,662 yd³ of concrete placed to date
 - = 22.9 million lbs
 - = 20.7 miles of typical sidewalk



UPCOMING SCHEDULE MILESTONES

- East Cottages Slab on Grade Starts 10/15/18
- East Apartments (B6) Slab on Grade Complete 10/16/18
- East Apartments (B6) Panelized Framing Starts 10/17/18
- West Apartments (B5) Slab on Grade Complete 11/06/18
- West Apartments (B5) Panelized Framing Starts 11/13/18
- Clubhouse (B4) Slab on Grade Complete 11/28/18
- Clubhouse (B4) Panelized Framing Starts 12/04/18

31,018

SAFETY HOURS
TO DATE

PROJECT PHOTOS

September 2018





NW Podium Deck reinforcement and formwork



NW Podium Deck reinforcement and formwork



NW Podium Deck Pour - Pump



NW Podium Deck pour – pump/screed



NW Podium Deck pour – pump/screed



NW Podium deck pour - finishing



NW Podium deck pour - finishing



Podium Deck Complete



B5 foundation excavation



B6 foundation reinforcement



B6 grade beam reinforcement



B6 foundation reinforcement





Memory Care - Steel Erection



Memory Care – fire retardant paint application



Memory Care - panelized wall delivery



Memory Care – panelized wall placement



Memory Care - panelized wall placement



Memory Care – structural steel and panelized wall placement



E Cottages - foundation layout



E cottages - foundation excavation



E Cottages - UG plumbing layout




E Cottages - foundation excavation and finish Grade



Virtual Design Coordination

- Current Coordination Status:


- Garage (B1)Complete
- Memory Care (B2).....Complete
- Apartments (B5/B6).....In Progress
- Clubhouse (B4).....In Progress
- Restaurant (B3)Upcoming

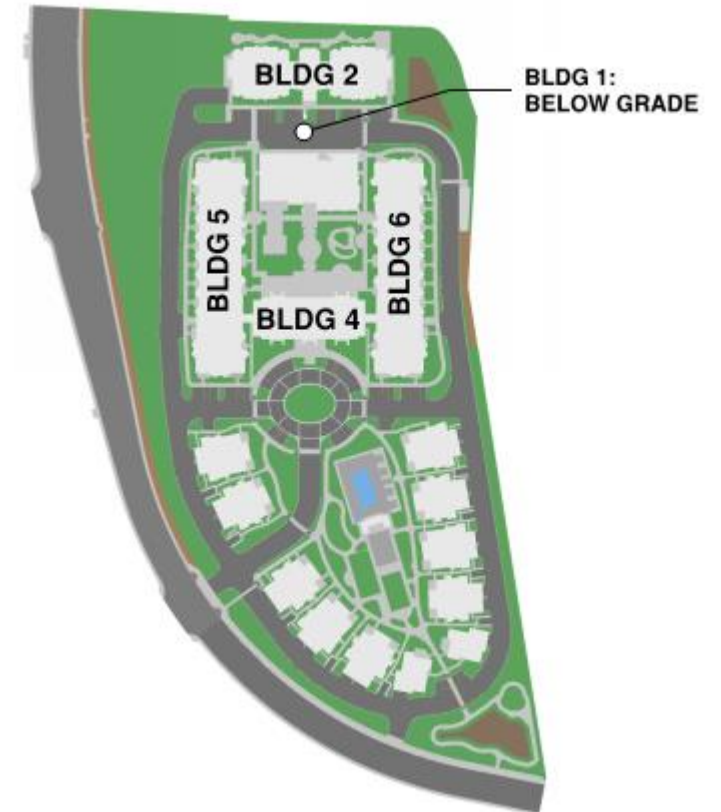



Time-Lapse

Time-Lapse of B2 NW Podium Pour - [Click here to view](#)

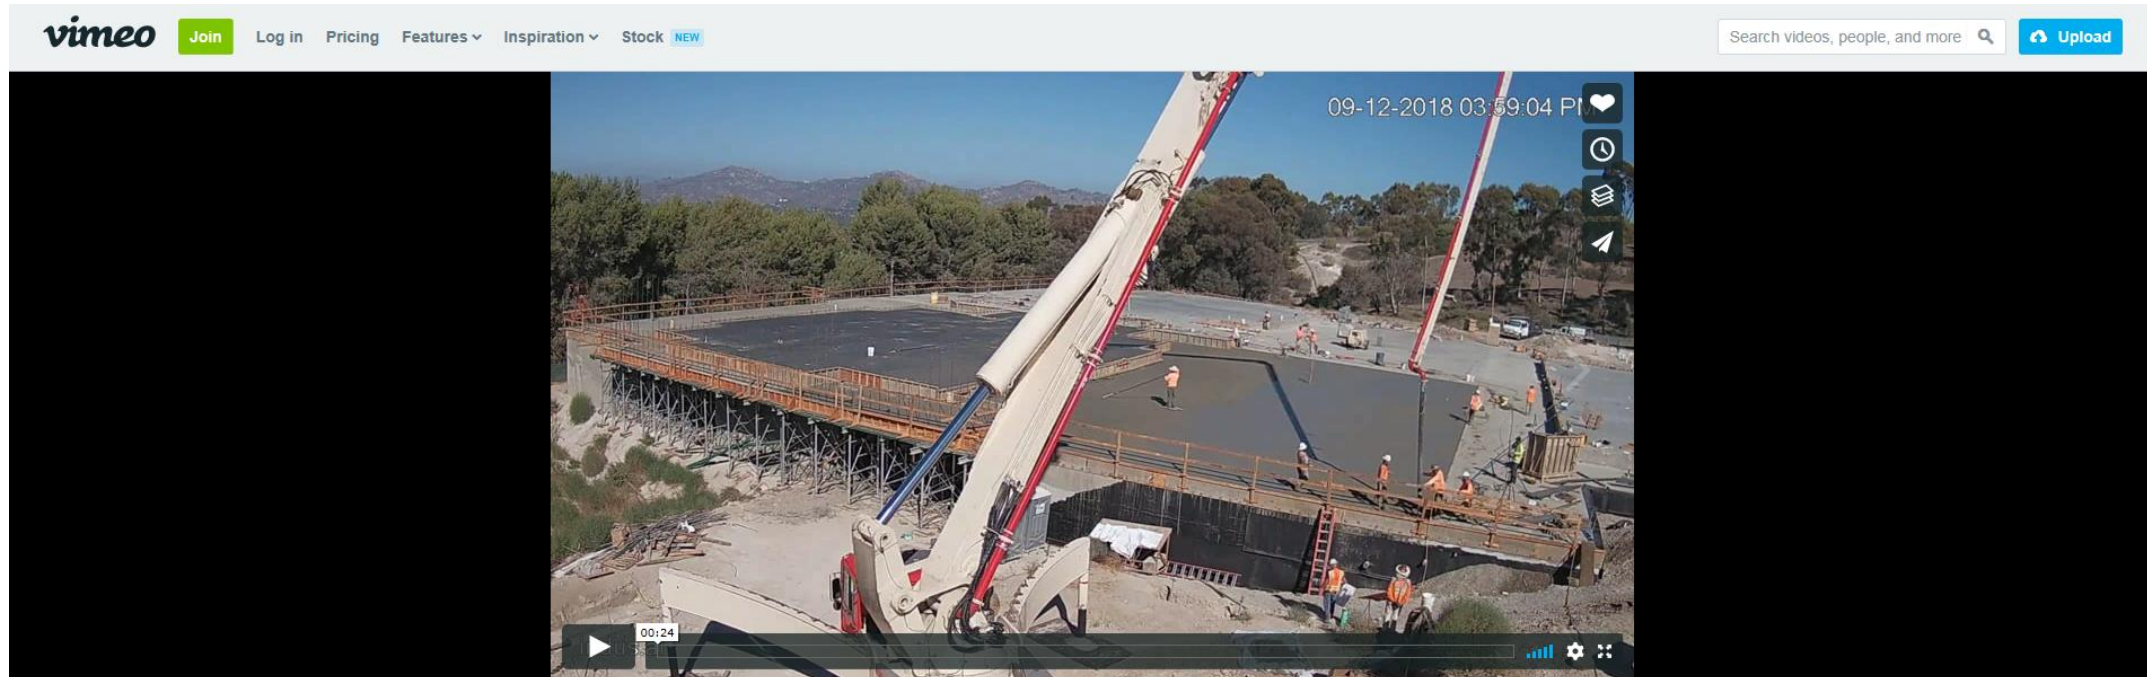

Silvergate - NW Podium Pour 9/12/18

Related Videos
☒ Autoplay next video

Note: If you are having trouble accessing the video link, please copy and paste the direct address as follows into your browser: <https://vimeo.com/294041159>



UPCOMING HIGHLIGHTS

- East Apartments (Building 6)
 - N Grade beam/foundation pour
 - Slab on grade grading, formwork, reinforcement, and pour
- N Podium Deck (Buildings 1 & 2)
 - Structural Steel/Panelized Framing Installation
- West Apartments (Building 5)
 - Grade beam/foundation reinforcement and pour
 - Slab on grade grading, formwork, reinforcement, and pour
- Clubhouse (Building 4)
 - Rough grading, plumbing and foundation excavation
 - Underground Plumbing & Electrical installation
- Cottages (Buildings 7-9)
 - Rough grading, plumbing and foundation excavation
 - Underground Plumbing & Electrical installation
 - Slab on grade formwork, reinforcement, and pour



CONTACT INFORMATION

TEAM CONTACT:

Hans Muecke

Vice President of Construction

(p) 858-812-7964

(c) 630-606-2503

Hans.Muecke@ryancompanies.com

Keith Pitts

Senior Project Manager

(p) 858-812-7970

(c) 619-385-9587

Keith.Pitts@ryancompanies.com

Travis Ürig

Project Manager

(p) 858-812-79

(c) 602-329-2044

Travis.Urig@ryancompanies.com

Michael Beadle

Division Manager

(p) 858-812-7970

(c) 619-385-9587

Keith.Pitts@ryancompanies.com

Cody Vander Veen

Project Manager

(p) 858-812-7953

(c) 619-385-9587

Cody.VanderVeen@ryancompanies.com

Jerame Carlson

Project Engineer

(p) 858-812-7951

(c) 641-231-1208

Jerame.Carlson@ryancompanies.com

Heather Sullivan

Project Coordinator

p) 858-812-7963

Heather.Sullivan@ryancompanies.com

FIELD CONTACT:

Nick Cap

Superintendent

(p) 858-812-7961

(c) 602-513-3235

Nick.Cap@ryancompanies.com

Paul Stykel

Superintendent

(c) 619-385-1115

Paul.Stykel@ryancompanies.com
