

PROJECTIVE PDATE

Silvergate Rancho Bernardo

San Diego, CA

January 2019

TABLE OF CONTENTS

- Current Highlights
- Safe Hours
- Fun Fact
- Project Photos
- Upcoming Highlights
- Ryan Companies Contact Information






CURRENT HIGHLIGHTS

- Memory Care (Building 2)
 - Roof Joists and roof decking completed
 - Roof trusses in progress
 - L1 interior framing and MEP rough-in in progress
- East Apartments (Building 6)
 - L1 framing interior walls in progress
 - L2 panelized walls completed
 - L2 ceiling joists in progress
- West Apartments (Building 5)
 - Intumescent paint application completed
 - L1 panelized walls in progress
- Clubhouse (Building 4)
 - Concrete foundation poured
 - Structural steel started

- E Cottages (7D, 7E, 8C, 8D, 9B)
 - Roofing dry-in and TPO roofing completed
 - MEP&F rough-in in progress
- SW Cottages (7B, 8B, 7C, 9A)
 - Roofing dry-in and TPO roofing completed
 - MEP&F rough-in in progress
- W Cottages (7A, 8A)
 - Concrete slab poured
- Poolhouse (Building 10)
 - Concrete slab poured







SAFETY HOURS TO DATE

Fun Fact: Our safe hours to date are equivalent to one person working full time for **37 years** and **4 months**!




PROJECT PHOTOS









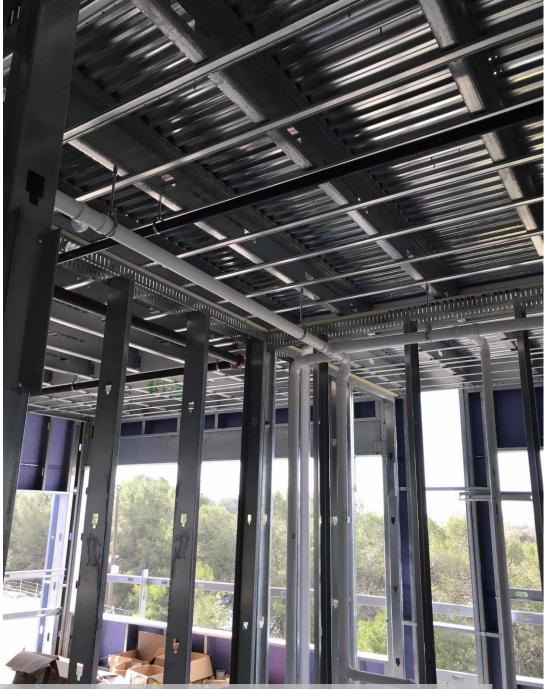






Building 2 - L2 plumbing and fire protection piping







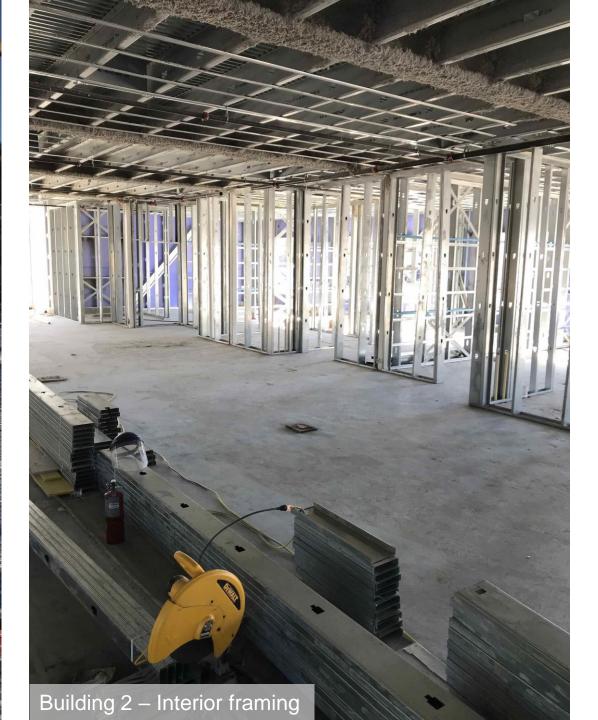





Building 10 layout, SW Cottages roofing dry-in










Building 4 – Steel erection.. January 21st









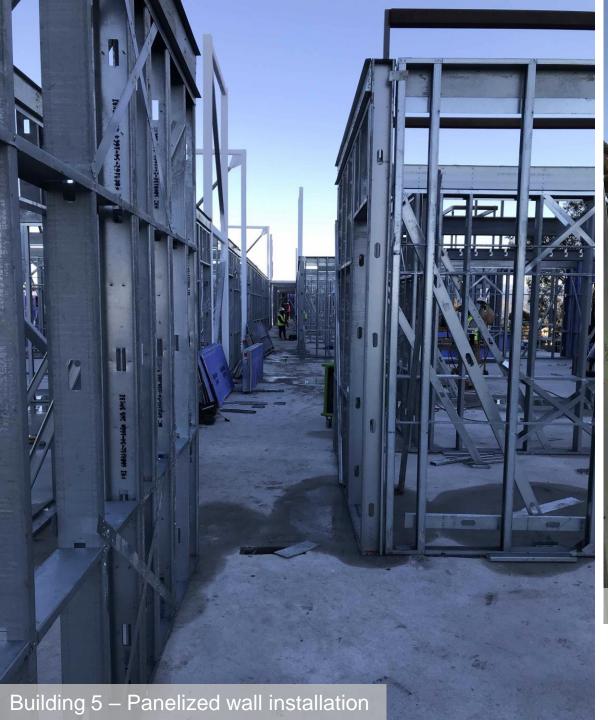



RYAN

















UPCOMING HIGHLIGHTS

- East Apartments (Building 6)
 - L1 and L2 interior framing and MEP&F rough-in
 - L3 concrete deck pour
 - L3 panelized wall framing and roof joists
- Memory Care (Building 2)
 - L1 and L2 MEP&F rough-in
 - Roof joists and metal deck completion
 - Roof MEP penetrations and Roofing start
- West Apartments (Building 5)
 - L1 panelized wall framing
 - L1 interior framing and MEP&F rough-in
 - L2 concrete deck pour
 - L2 panelized wall framing
- Clubhouse (Building 4)
 - Structural Steel Erection and metal deck installation

- E Cottages (7D, 7E, 8C, 8D, 9B)
 - MEP&F rough-in completion
 - Window and door installation
 - Roof concrete tile installation
- SW Cottages
 - MEP&F rough-in
 - Window installation
 - Roof concrete tile installation
- W Cottages
 - Wall framing and roof trusses
- Pool House (Building 10)
 - Wall framing and roof trusses





CONTACT INFORMATION

TEAM CONTACT:

Hans Muecke

Vice President of Construction (p) 858-812-7964 (c) 630-606-2503 Hans.Muecke@ryancompanies.com

Keith Pitts

Senior Project Manager (p) 858-812-7970 (c) 619-385-9587 Keith.Pitts@ryancompanies.com

Travis Ürig

Project Manager (p) 858-812-7920 (c) 602-329-2044 Travis.Urig@ryancompanies.com

Heather Sullivan

Project Coordinator (p) 858-812-7963 Heather.Sullivan@ryancompanies.com Michael Beadle Division Manager (p) 858-812-7926 (c) 612-239-5547 Michael.Beadle@ryancompanies.com

Cody Vander Veen Project Manager (p) 858-812-7953 (c) 612-400-5121 Cody.VanderVeen@ryancompanies.com

Jerame Carlson

Project Engineer (p) 858-812-7951 (c) 641-231-1208 Jerame.Carlson@ryancompanies.com

Luis Valdovinos

Project Engineer (p) 619-318-9471 Luis.Valdovinos@ryancompanies.com Nick Cap Superintendent (c) 602-513-3235 Nick.Cap@ryancompanies.com

Paul Stykel Superintendent (c) 619-385-1115 Paul.Stykel@ryancompanies.com

Tommy Sewell Assistant Superintendent (c) 619-380-1203 Tommy.Sewell@ryancompanies.com

Katerina Grengs Virtual Design Coordinator (p) 612-492-4713 (c) 651-472-1915 Katerina.Grengs@ryancompanies.com Courtney Carr Project Engineer Intern (c) 612-532-7074 Courtney.Carr@ryancompanies.com

