



PROJECT UPDATE


Silvergate Rancho Bernardo
San Diego, CA

August 2019

TABLE OF CONTENTS

- Site Map
- Safety Hours
- Current Highlights
- Project Photos
- 360 Photos
- Upcoming Highlights
- By the Numbers
- Ryan Companies Contact Information



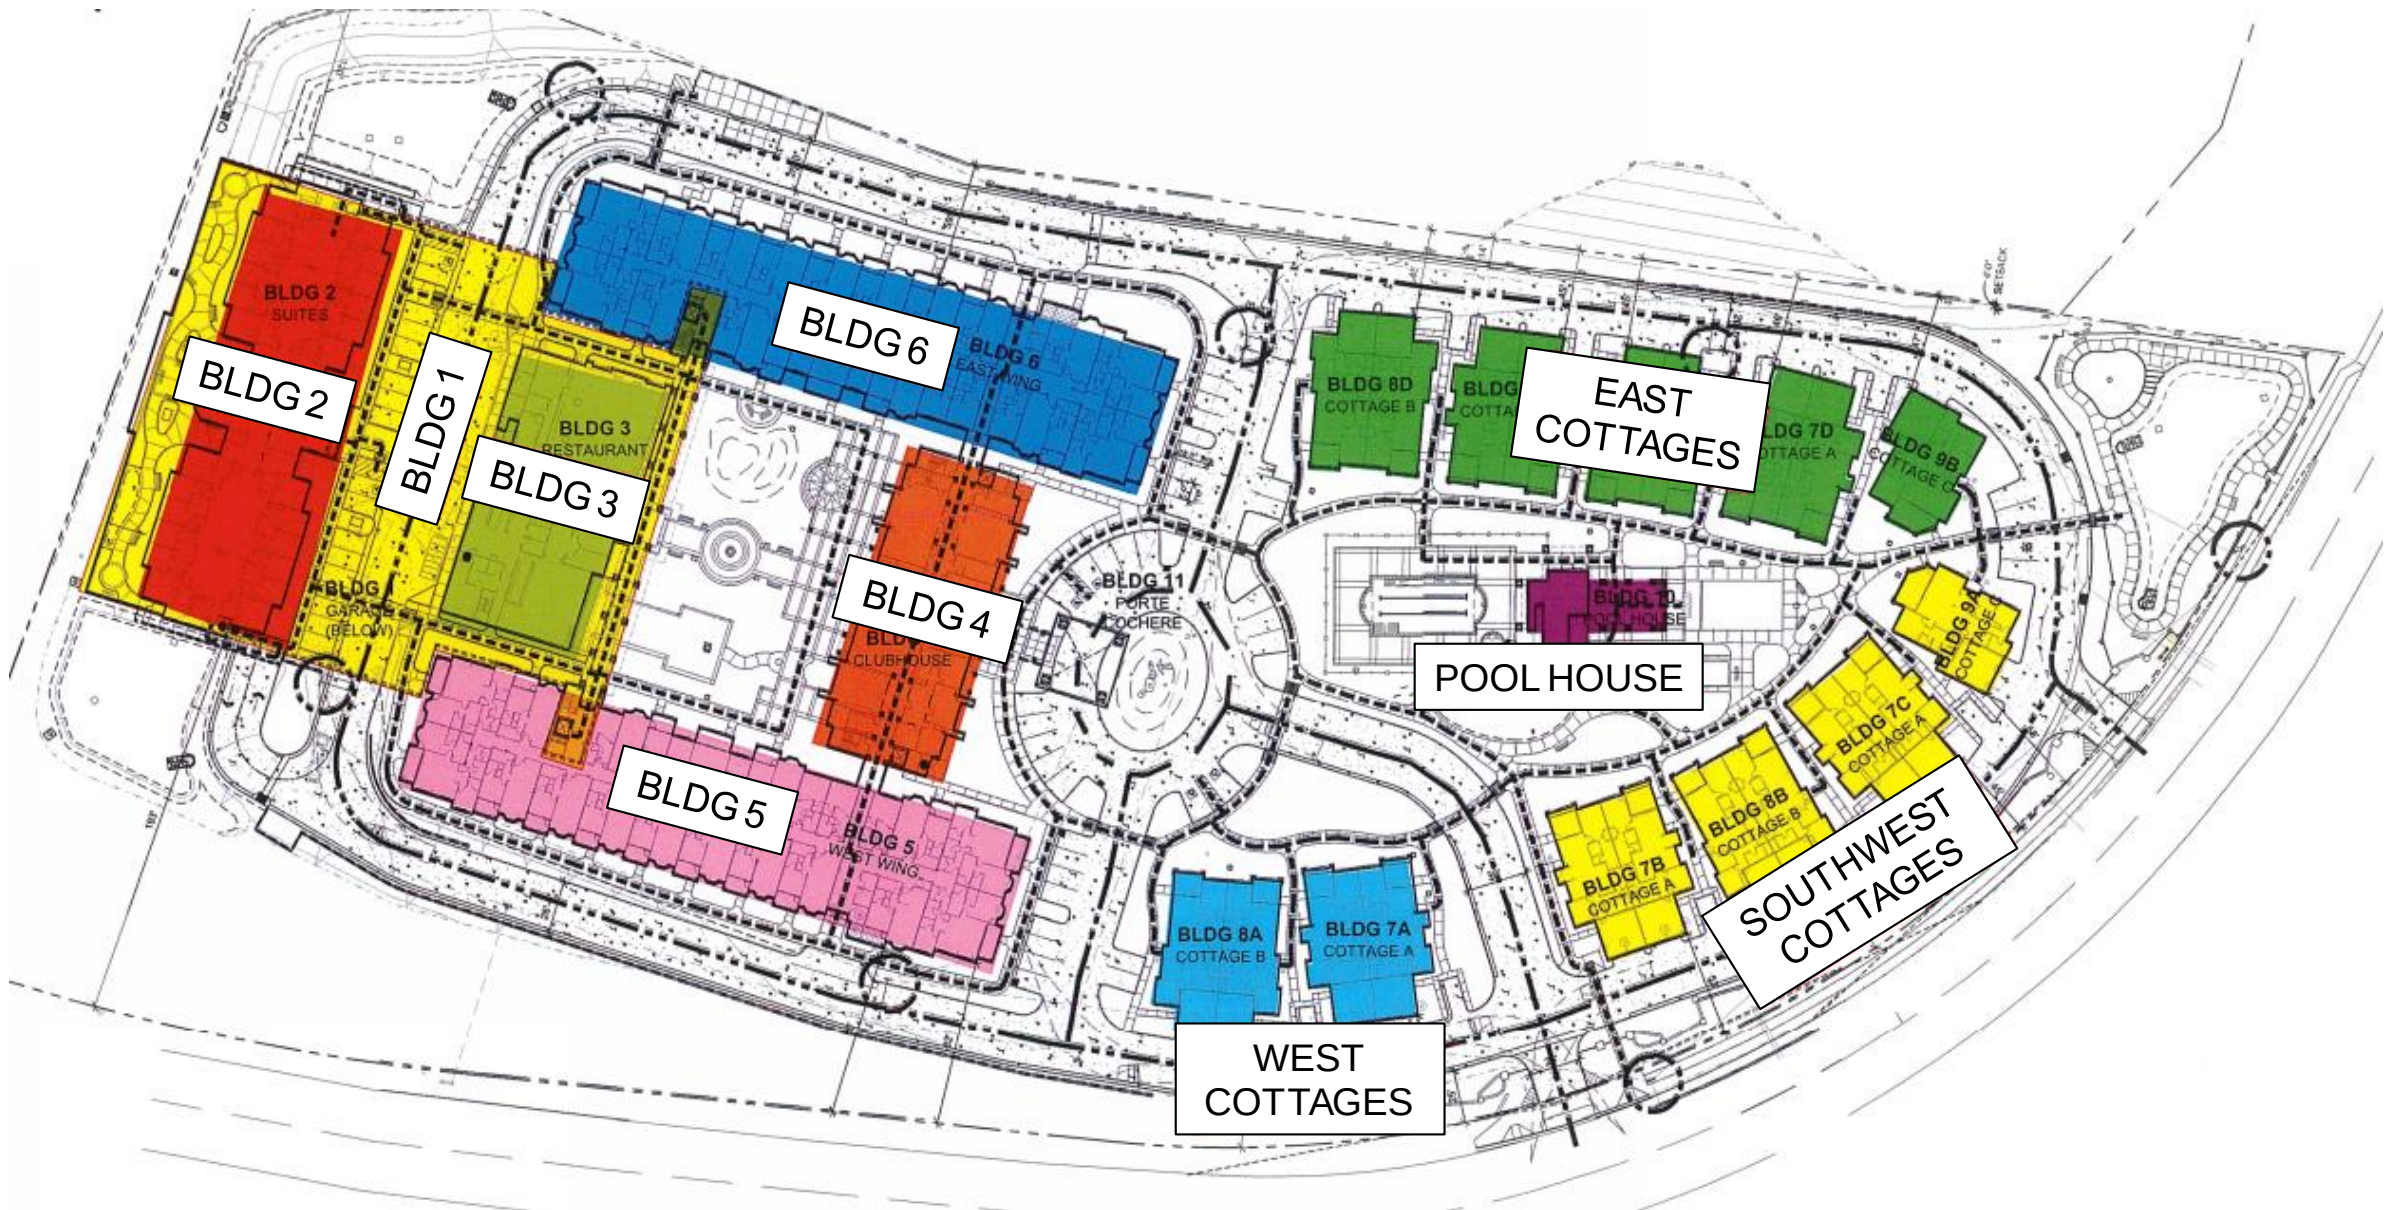

216,091+

SAFETY HOURS TO DATE

Current Highlights

- Memory Care (Building 2)
 - Starting shower waterproofing on Level 2
 - Cabinets & countertops have been installed on Level 2
 - Priming & 1st coat of paint on Level 1
 - Hanging drywall in grey water & boiler rooms
- Restaurant & Colonnade (Building 3)
 - Framing fireplace in main dining room
 - All plywood for roof installed
 - Continue MEP rough-in
 - Starting to hang interior drywall
- Clubhouse (Building 4)
 - Continue framing & MEP rough on Level 3
 - Roof is complete
 - Porte Cochere fire sprinkler rough-in
- West Apartments (Building 5)
 - All windows installed
 - Phase 2 of MEP rough in progress
 - Production drywall & insulation in progress
 - Taping to follow
- East Apartments (Building 6)
 - Hanging soffits on Level 1
 - Exterior lath in progress
 - Milestone - All drywall hung
- Cottages (Buildings 7A-E; 8A-D; 9A,B)
 - Installing interior doors & garage doors
 - Patio concrete all poured
 - Continuing MEP Trim install
- Porte Cochere & Walkway
 - Roofing finishing
 - Starting electrical & fire installation
- Pool House (Building 10)
 - Stone veneer complete
 - Completing MEP trim
 - Patio poured
- Sitework
 - Curbs poured on south side of site
 - Fine grading continues around cottages


PROJECT PHOTOS



MEMORY CARE







RESTAURANT




CLUBHOUSE & PORTE COCHERE



WEST APARTMENTS

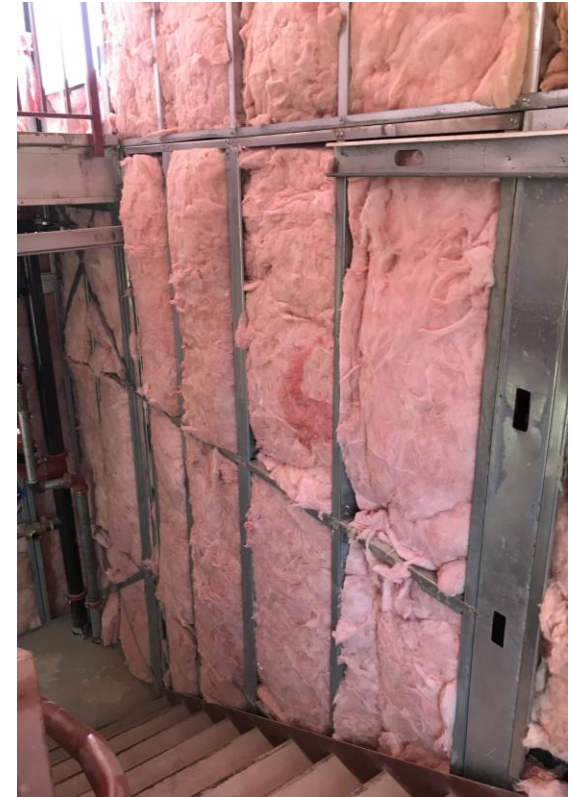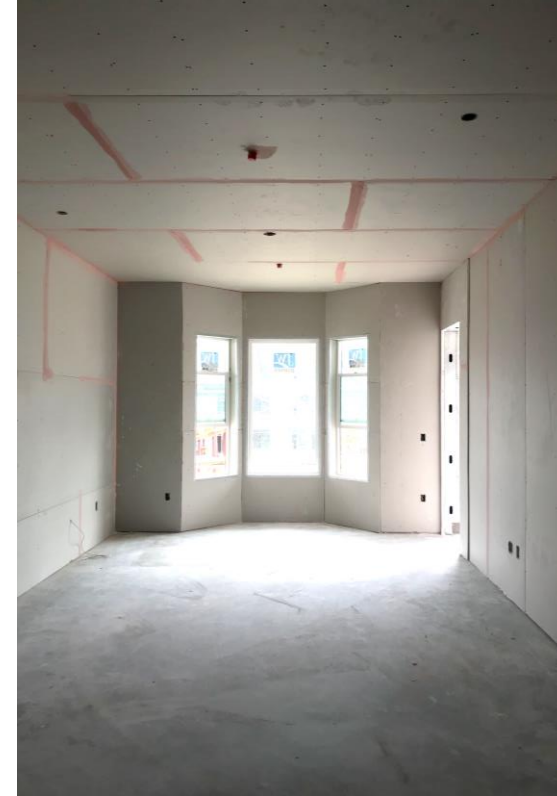


EAST APARTMENTS







COTTAGES






POOL HOUSE



360 PHOTOS

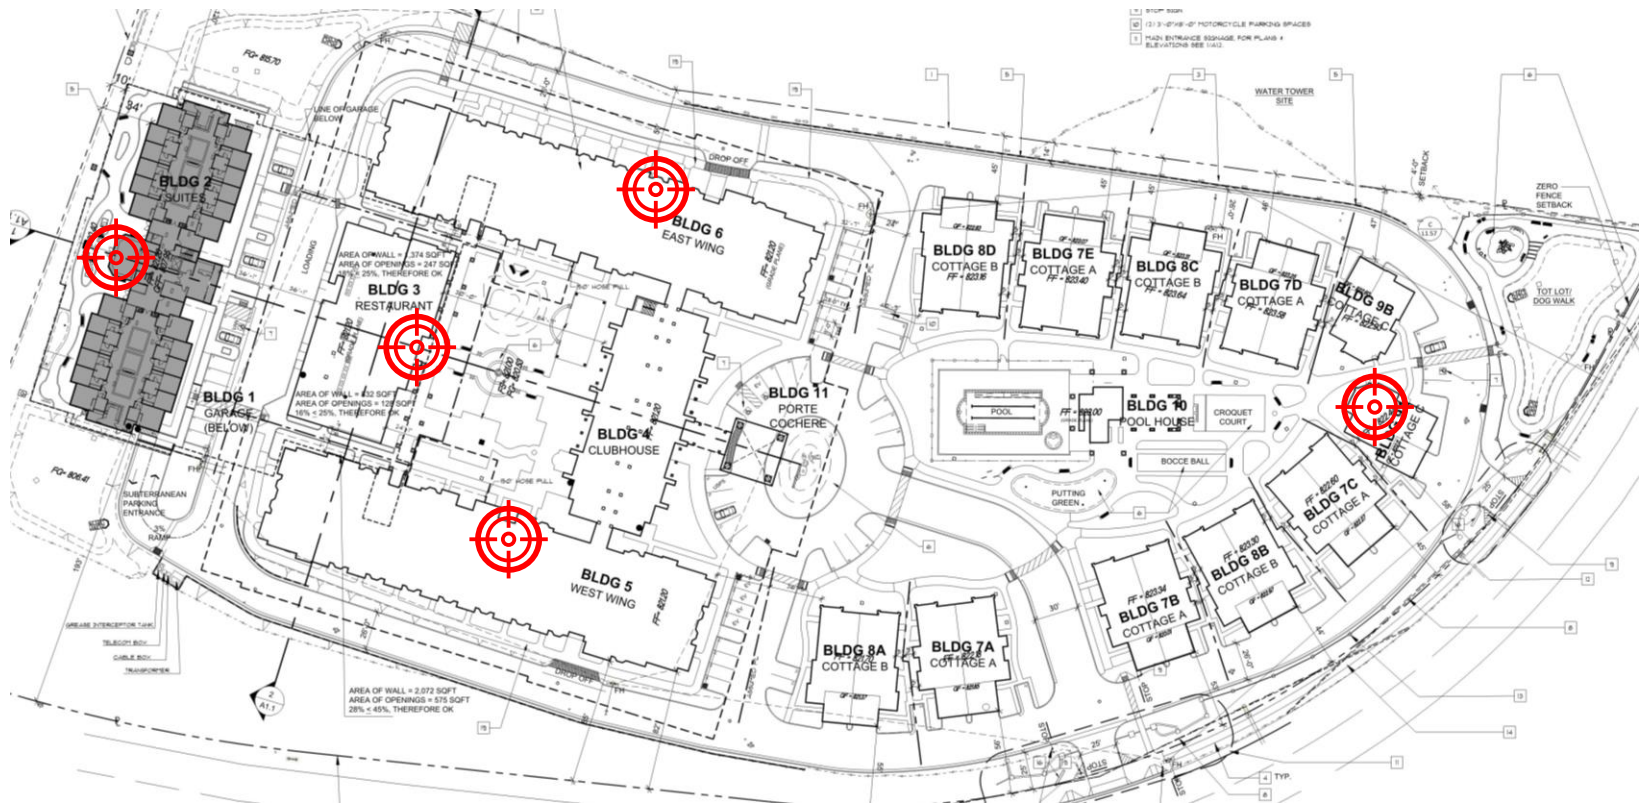

Click on the targets to view 360 degree images of the site.

The link will take you to your web browser to view the photo.

Then use your cursor to pan around the photo in any direction you like.

Upcoming Highlights

- Memory Care (Building 2)
 - Finish exterior stucco
 - Door installation on both levels
 - Continue installing finishes
- Restaurant & Colonnade (Building 3)
 - Continue working on exterior skin
 - Starting roofing tile & TPO
 - Additional structural framing at entry
- Clubhouse (Building 4)
 - Insulation to start
 - Continue interior framing & MEP rough on all levels
 - Complete second layer densglass
 - Hang soffits in Porte Cochere
- West Apartments (Building 5)
 - Complete installing doors & windows
 - Complete drywall installation & MEP Rough
- East Apartments (Building 6)
 - Start exterior stucco
 - Continuing drywall sequence on all levels
 - Completing soffits on level 1
 - Hanging soffits on levels 2 & 3
- Cottages (Buildings 7A-E; 8A-D; 9A,B)
 - Complete tile installation & starting flooring
 - Complete doors & trim
 - Turn over model unit to owner
 - Pouring sidewalks between cottages
- Porte Cochere & Walkway
 - Start electrical & fire installation
 - Install precast columns
- Pool House (Building 10)
 - Start interior paint
 - Complete MEP installation
 - Continue tile installation

By the Numbers

- Drywall - hung 190,000+ SF in building interiors
- Roofing – installed 82,540 SF of concrete tiles
- Windows – installed 480 windows
- Sitework – poured 1650 linear feet of curb on south side of site
- Flooring - 18,000+ SF will be installed in the cottages within the next month

Contact Information

Hans Muecke
Senior VP Operations Western US
(p) 858-812-7964
(c) 630-606-2503
Hans.Muecke@ryancompanies.com

Michael Beadle
Director of Construction
(p) 858-812-7926
(c) 612-239-5547
Michael.Beadle@ryancompanies.com

Niels Zwinkels
Field Coordinator
(p) 858-812-7910
(c) 760-815-0615
Niels.Zwinkels@ryancompanies.com

Keith Pitts
Project Executive
(p) 858-812-7970
(c) 619-385-9587
Keith.Pitts@ryancompanies.com

Travis Urig
Project Manager
(p) 858-812-7920
(c) 602-329-2044
Travis.Urig@ryancompanies.com

Cody Vander Veen
Project Manager
(p) 858-812-7953
(c) 612-400-5121
Cody.VanderVeen@ryancompanies.com

Jerame Carlson
Senior Project Engineer
(p) 858-812-7951
(c) 641-231-1208
Jerame.Carlson@ryancompanies.com

Katerina Grengs
Virtual Design Coordinator
(p) 612-492-4713
(c) 651-472-1915
Katerina.Grengs@ryancompanies.com

Nick Cap
Superintendent
(c) 602-513-3235
Nick.Cap@ryancompanies.com

Paul Stykel
Superintendent
(c) 619-385-1115
Paul.Stykel@ryancompanies.com

Ed Souza
Superintendent
(c) 858-245-4874
Ed.Souza@ryancompanies.com

Tommy Sewell
Assistant Superintendent
(c) 619-380-1203
Tommy.Sewell@ryancompanies.com

Heather Sullivan
Project Coordinator
(p) 858-812-7963
Heather.Sullivan@ryancompanies.com

Taylor Barton
Project Engineer
(p) 607-425-0101
Taylor.Barton@ryancompanies.com

Allie Shank
Project Engineer Intern
(c) 209-303-6360
Allie.Shank@ryancompanies.com

Ahad Ali
Project Engineer Intern
(c) 619-888-9153
Ahad.Ali@ryancompanies.com
